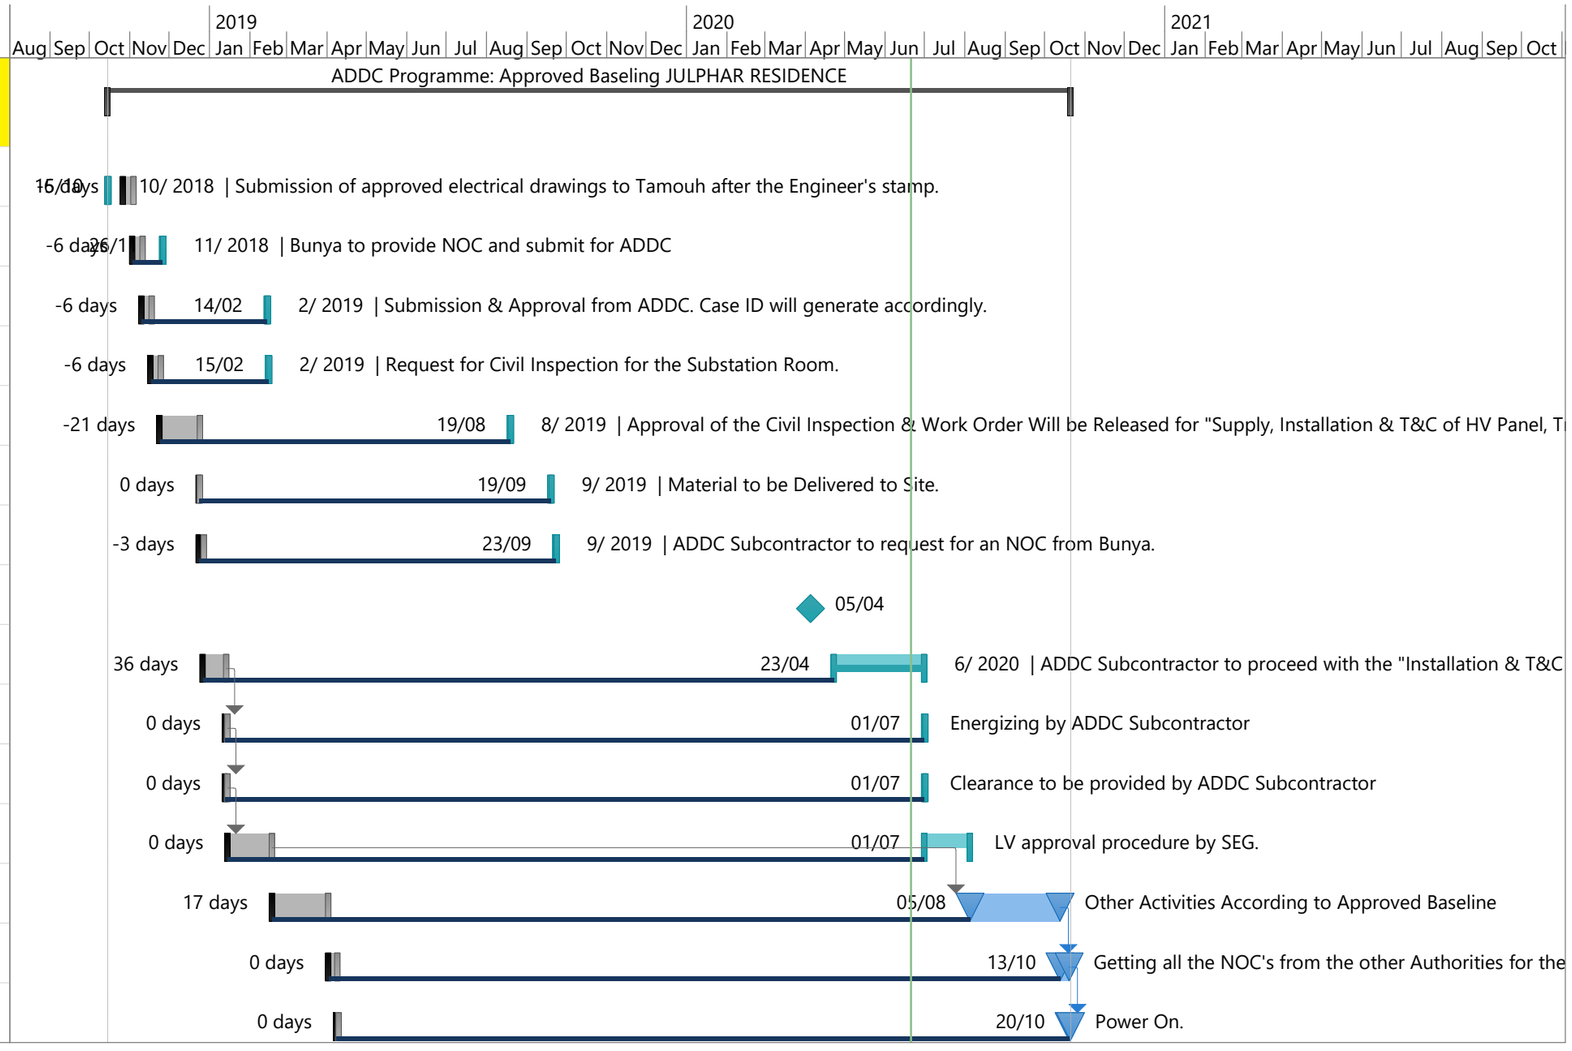ID		WBS	Task Name	Baseline Start	Baseline Finish	Actual Start	Actual Finish
1		1	**ADDC Programme: Approved Baseling JULPHAR RESIDENCE**	27/10/18	08/04/19	15/10/18	**NA**
2	✓	1.1	Submission of approved electrical drawings to Tamouh	27/10/18	03/11/18	15/10/18	15/10/18
3	✓	1.2	Bunya to provide NOC and submit for ADDC	03/11/18	10/11/18	26/11/18	26/11/18
4	✓	1.3	Submission & Approval from ADDC. Case ID will generate	10/11/18	17/11/18	14/02/19	14/02/19
5	✓	1.4	Request for Civil Inspection for the Substation Room.	17/11/18	24/11/18	15/02/19	15/02/19
6	✓	1.5	Approval of the Civil Inspection & Work Order Will	24/11/18	24/12/18	19/08/19	19/08/19
7	✓	1.6	Material to be Delivered to Site.	24/12/18	24/12/18	19/09/19	19/09/19
8	✓	1.7	ADDC Subcontractor to request for an NOC from	24/12/18	27/12/18	23/09/19	23/09/19
9	✓	1.8	Approval from Bunya. " Providing the NOC "	27/12/18	27/12/18	05/04/20	05/04/20
10	✓	1.9	ADDC Subcontractor to proceed with the "Installation	27/12/18	13/01/19	23/04/20	30/06/20
11		1.10	Energizing by ADDC Subcontractor	13/01/19	14/01/19	NA	NA
12		1.11	Clearance to be provided by ADDC Subcontractor	13/01/19	14/01/19	NA	NA
13		1.12	LV approval procedure by SEG.	15/01/19	17/02/19	NA	NA
14		1.13	Other Activities According to Approved Baseline	18/02/19	01/04/19	NA	NA
15		1.14	Getting all the NOC's from the other Authorities for the BCC.	02/04/19	08/04/19	NA	NA
16		1.15	Power On.	08/04/19	09/04/19	NA	NA
